

Refurbishment Progress Report August 2009



External Facade



External Façade with new Curtain Wall System is around 70% completed:

1.	Front Façade	Completed
2.	Rear Facade	65%
3.	Side Façade #1 (next to Kompleks Antarabangsa)	Completed
4.	Side Façade #2 (facing Equatorial Hotel)	85%

Main Entrance

The new Main Driveway is around 80% completed. The new Infinity Pool is currently under construction.



Main Entrance



Artist Impression

Main Lobby

The Main Lobby is around 80% completed. The Executive Lounge is targeted to open in October.



Before



After



Executive Lounge



Artist Impression

Secondary Lobby

- ❑ The new Secondary Lobby at Jalan Perak is around 70% completed. Opening is expected in Jan 2010 (after Authority Approval).



Before



Work progress

Secondary Lobby

Level P2A, Internal view



Lift Installation




Floor Tiling



Mechanical & Electrical System

❑ New Building Automation System is 70% completed.

❑ New Air-Handling Units (AHU) have been fully installed.

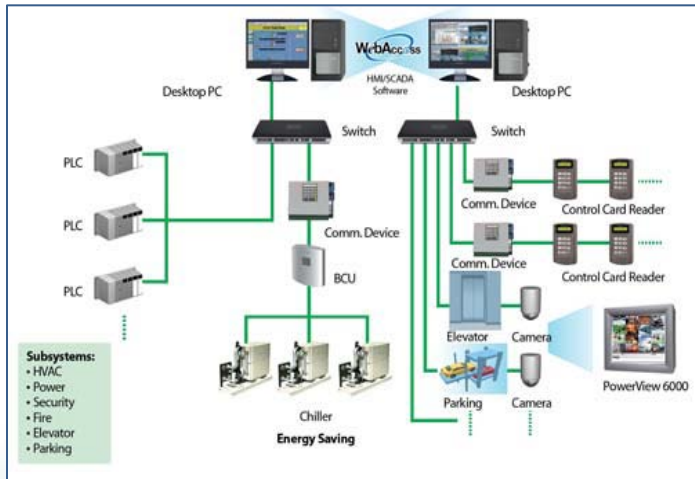

Ledge Conversion



After



Work in progress

Next Milestones

1.	Phase 1 completion (all areas except for Internal Ledge Conversions)	30 October 2009
2.	Final completion	31 December 2009





Thank you for your cooperation.
